



LED lighting rollout

CITY OF MARION

12th July



Percentage lights completed

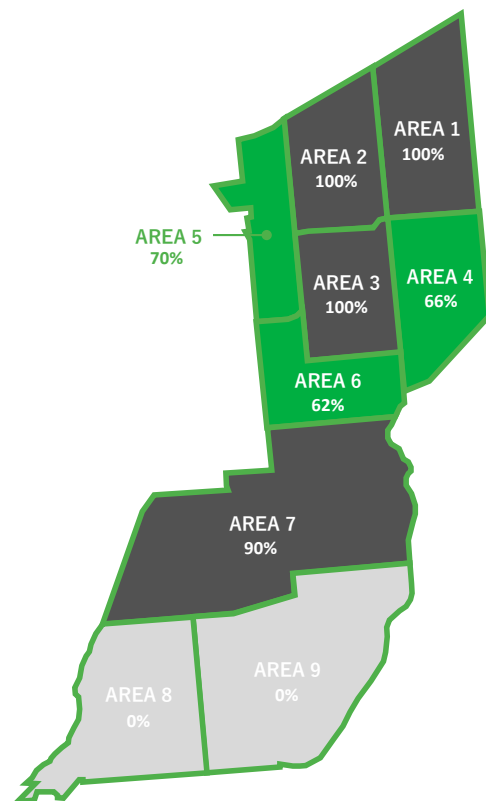

Planned start dates

Areas	Area 1	Area 2	Area 3	Area 4	Area 5	Area 6	Area 7	Area 8	Area 9
Start date	Comp	Comp	Comp	May	May	June	July	Aug	Sept



55%
complete

PROGRESS REPORT

Total lights	8,792
Completed	4824
