



LED lighting rollout

30 November 2018

CITY OF NORWOOD, PAYNEHAM, ST PETERS




Percentage lights completed

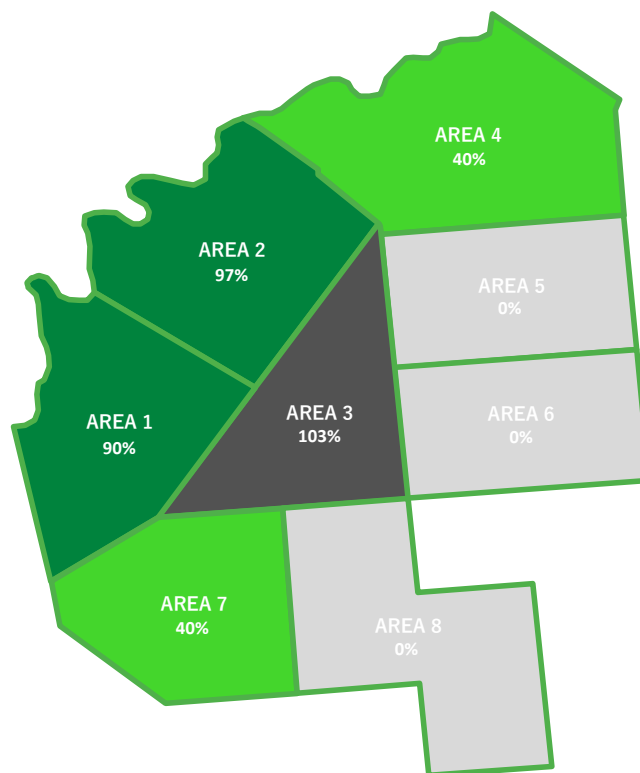

Planned start dates

Areas	Area 1	Area 2	Area 3	Area 4	Area 5	Area 6	Area 7	Area 8
Start date	01-Sep	01-Sep	01-Oct	01-Oct	01-Oct	01-Nov	01-Nov	01-Nov

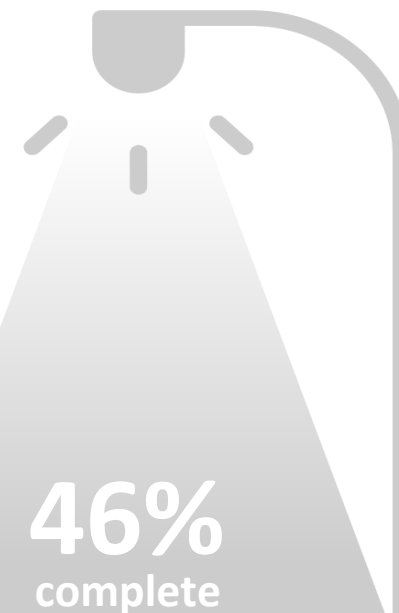

PROGRESS REPORT

Total lights	2,867
Completed	1333
