LED lighting rollout

CITY OF CHARLES STURT

7 September 2018

Percentage lights completed

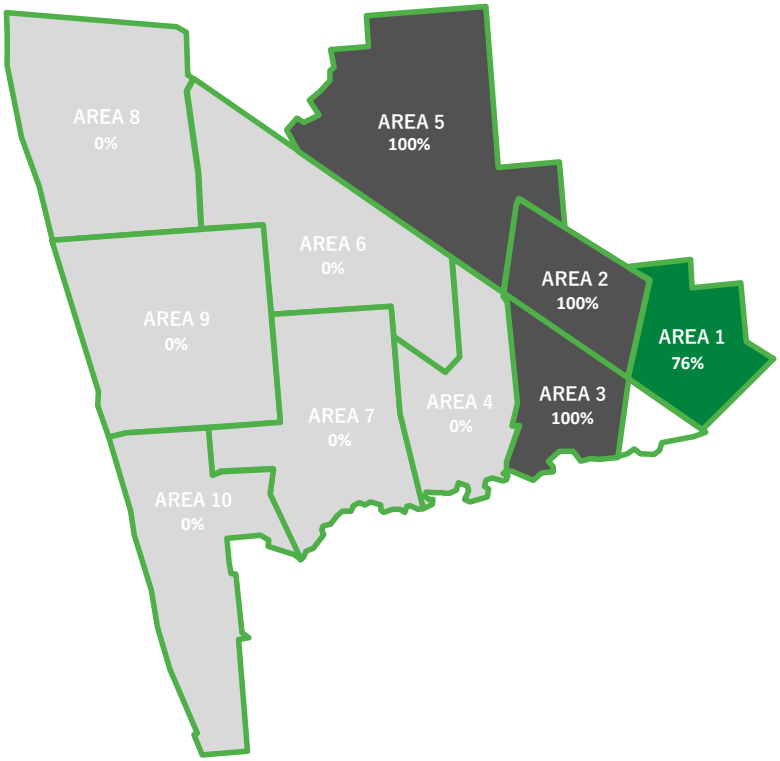



Planned start dates

Areas	Area 1	Area 2	Area 3	Area 4	Area 5	Area 6	Area 7	Area 8	Area 9	Area 10
Start date	01-Apr	01-Apr	01-Apr	TBA	July	TBA	TBA	TBA	TBA	TBA

32%
complete

PROGRESS REPORT

Total lights	8,162
Completed	2600
