LED lighting rollout

18 May 2018

CITY OF MARION

Percentage lights completed

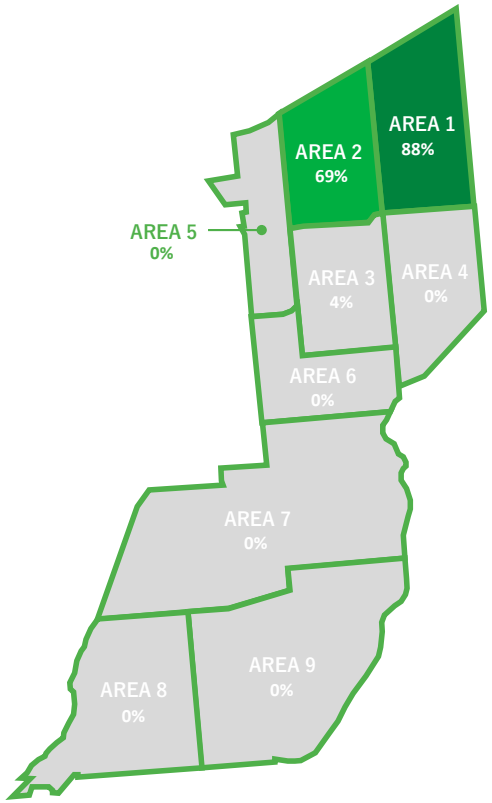



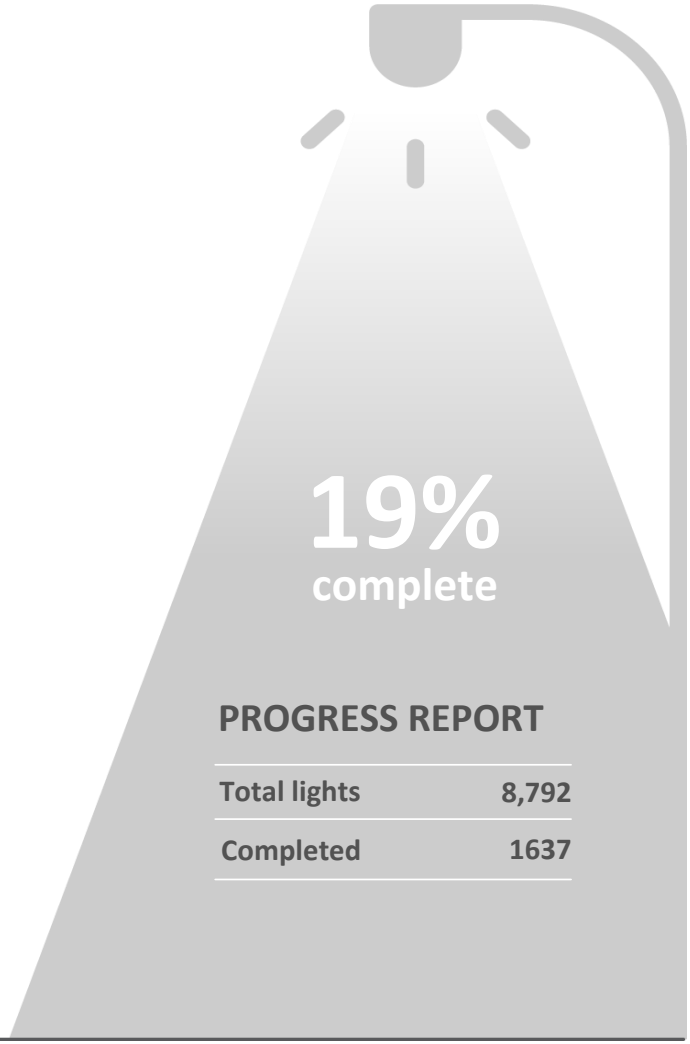

PROGRESS REPORT

Total lights	8,792
Completed	1637

Planned start dates

Areas	Area 1	Area 2	Area 3	Area 4	Area 5	Area 6	Area 7	Area 8
Start date	March	April	May	TBA	TBA	TBA	TBA	TBA
